
Group Participation Sheet

Prof. Mouhamed Abdulla, School of Applied Computing, FAST
Sheridan College Institute of Technology and Advanced Learning, GTA, ON, Canada

A portion of this course is devoted to group work. This **Group Participation Sheet** (GPS), hereinafter referred to as the **GPS Sheet**, will specifically indicate the group members that actively contributed to the assignment, lab project, deliverable, or report. All names indicated on this GPS sheet will receive the same grade for the attached group work. Group members with names and signatures not shown on this GPS sheet will receive a grade of "**zero**" for the mentioned assessment. Any concerns regarding this matter should be brought to the professor's attention by the team leader prior to the submission deadline.

Please fill the table below electronically. Group members that participated in this evaluation should **write their names** and append their **signature**. The signed GPS sheet should be added as the **first page of all group evaluations**. This should be **applied** to all evaluations uploaded on SLATE as **softcopy**, and printed/stapled and presented as **hardcopy** to your professor.

Clear Form Print Form

Course Title:	INFO-53883 - AI/ML Capstone Project	
Evaluation Name:	INFO-53883 - D2 (15%, Group Work, Project Design Doc.)	
Team Number:	INFO-53883 (AI/ML Capstone) - Team 3B	
Referencing and Citation Style:	*APA Style* ○ *IEEE Style* ○ *N/A* ●	
Group Members:	*First Name and Family Name of group members:*	*Signature of group members:*
	(1) Binil John (team leader)	
	(2) Anisha chaudhary	
	(3) Karishma shaik	
	(4) Harmanjit singh	
	(5)	
Submission Date:	Oct 7th	

Any form of plagiarism and use of AI generated text in any part of your deliverable will result in a grade of zero for all members in the group. Teams involve in this form of academic misconduct will be reported for further disciplinary actions.

Grade:	/ 15

AI/ML Capstone Project

D2 – Project Design Document (15% of final mark)

Due: Week 4 (softcopy on SLATE, hardcopy to your Professor in class)

Name 1: _____Binil John_____ Student Number 1: ___991844827_____

Name 2: _____Anisha chaudh_____ Student Number 2: ___991853183_____

Name 3: _____Karishma shaik_____ Student Number 3: ____991838246_____

Name 4: _____Harmanjit singh_____ Student Number 4: ____991839129_____

Name 5: _____ Student Number 5: _____

Instructions:

- Please work on the following deliverable with your group.
- Prepare your deliverable report as discussed in class.
- Type your report using word processing software (preferably using LaTeX, otherwise MS Word is fine).
- Upload your report in PDF format on SLATE. Team leader should upload this deliverable on SLATE as a single PDF file.
- Present a printout (stappled) of your deliverable to your Professor in class in **Week 4**.

Overall Objective:

In this "**D2 – Project Design Document**", the objective is to design a *realistic* and *achievable* project plan that defines technical architecture, milestones, and team deliverables using industry-standard practices. This document will serve as a foundational blueprint for all subsequent development phases, and it must be structured with clarity and professionalism.

Q1: Project Objectives

Create a **Work Breakdown Structure (WBS)** detailing technical tasks and deliverables. As part of your WBS, you will need to include at least **four Work Packages (WPs)**. These WPs should address the major objectives of the AI/ML system architecture and data flow you intend to work on in this capstone project. In the space below, provide an explicit heading for each WP followed by a brief description detailing what exactly you want to accomplish (in 4-6 sentences). [**2 marks**]

WP1 – Dataset Collection and Pre-processing

The first work package focuses on creating suitable dataset for the project. we will gather raw traffic sign image data specific to Ontario through manual image capturing and by selecting relevant images from open source datasets available on platform such as Kaggle or roboflow. The collected images will be organized according to respective class.Each image will then

be manually annotated using bounding boxes and class labels will be performed using tools like roboflow or labellmg, followed by quality checking. After the initial dataset is prepared, data augmentation techniques such as rotation, contrast adjustment, blurring and cropping will be applied to increase the dataset size.

WP2 -AI Model Development and Evaluation

The second work package focuses on developing and evaluating the traffic sign detection model. We will train our custom dataset using pretrained object detection model such as YOLO. The custom data set will be split into training, validation and testing sets to train and evaluate the model effectively while preventing overfitting. We have decided to train the model using two YOLO versions YOLOv8 and YOLOv11. The model hyperparameters will be fine tuned to achieve high accuracy and will select the best model by reviewing precision, recall and mAP. Incorrect and missed detections will be reviewed to identify areas for improving the model and retrain the model if needed.

WP3 – Real Time Detection and Driver Alert

The third work package focuses on connecting the model to real time camera pipeline. We will use OpenCV to handle the webcam video frames for processing. Trained YOLO model will detect traffic signs in realtime. The detected signs will be displayed through streamlit based user interface. when a sign is detected, text to speech library such as pyttsx3 or gTTs will be trigger instantly to generate an audio alert describing the detected sign. Testing and demonstration will be done using webcam and GPU enabled environment to support smooth real-time processing. For privacy protocols the live video feed never be stored.

WP4 - System Integration, Testing, and Final Demonstration

The forth work package focuses on combining the model, camera processing, audio feature and interface in a single working prototype. Will use github for source code management and seamless collaboration among the team members. The system will be tested inside a car with different traffic signs to identify functional and performance problems. Testing results will be used to make final adjustments. Finally, all the process and results will be used to prepare slides and other documentation for the final demonstration.

Q2: Project Tasks

The focus here is on identifying the granularity of the WPs. For each WP, develop at least **3-4 tasks** detailing the various subcomponents related to the AI/ML pipeline and applications. In the space below, provide a descriptive heading for each task. Then, for each labelled task, provide an explanation of what the task entails (in 1-2 sentences). Avoid being too redundant to what you indicated in **Q1**. [**2 marks**]

WP1– Dataset Collection and Pre-processing

• Data collection : field collection of Ontario traffic signs and selection of suitable sign classes from public dataset for the project.
• Data cleaning and organization : removing unsuitable, corrupted or duplicate images and organize them in different folders based on class for next step.
• Image annotation and class labelling : collected images will be annotated with bounding boxes and class labels will be assigned to each
• Data augmentation : Apply augmentation augmentation techniques such as rotation, contrast adjustment, blurring and cropping will be applied to increase the dataset size.

WP2-AI Model Development and Evaluation

• Dataset splitting and training preparation : The dataset will be split into training, validation and testing sets. The yolo training configurations and required parameters will be prepared.
• YOLOv8 and YOLOv11 model training : The prepared dataset will be used to train both the models to allow a fair comparison of their performance.
• Hyperparameter tuning and model evaluation : The hyperparameter of both the models will be fine tuned to improve performance. Precision, recall and mAP will be used to evaluate the models.
• Error analysis and model selection : errors in both the models will be reviewed and will try to improve the performance based on the evaluation results, better performing model will be selected at the end.

WP3– Real Time Detection and Driver Alert

•OpenCV webcam integration : integrating OpenCV to capture and process the incoming video frames in Realtime and stream them into detection pipeline.
• Realtime YOLO detection : The trained model will be integrated with the OpenCV pipeline to detect the signs from live video frames. Detected signs will be displayed with their bounding boxes and class labels.
• Audio alert generation : Implement an audio notification system using either pyttsx3 or gTTS. The audio alert will be triggered when a traffic sign is detected and will describe the detected sign.
• Streamlit interface development : A streamlit based interface will be developed to display the live camera feed and detection results.

WP4 - System Integration, Testing, and Final Demonstration

• Full system integration : combining the model, OpenCV camera pipeline, streamlit interface and audio alert into a single system.
• Functional and scenario testing : Testing the system in different scenarios and traffic sign examples to identify the functional issues.
• Performance testing : checking detection consistency , response time and the clarity of the alerts.
• Documentation and demonstration : prepare the final documents, results, repository, presentation and demo.

Q3: Task Owners

Assign roles and responsibilities for each team member. In other words, assign a "**task owner**" for each task within the WPs. This must be done *strategically* based on qualifications and interest of the team member being assigned a task. Common roles include, project manager, data engineer, AI/ML engineer, MLOps engineer, etc. Divide the workload equally among the team members so that it is fair, balanced, and realistic. In the space below, list the tasks from **Q2**, and indicate the name of the team member that will work on the specific task in parenthesis. Also, provide a specific description (in 1-2 sentences) why this specific team member is appropriate to work on the assigned task. [**1 mark**]

Anisha - Data Engineer - Annotation, dataset splitting, Streamlit interface, functional testing

Karishma - AI/ML Engineer - Augmentation, YOLO training, real-time detection, performance testing

Harmanjit - MLOps Engineer - Data cleaning, tuning and evaluation, OpenCV integration, full integration

Binil - Project Manager - Data collection, error analysis, audio alert, documentation and demo

WP1 – Data collection and Pre-processing

• Data collection (Binil): As a project manager, Binil can coordinate the field collection of Ontario signs and keep it on schedule.
• Data cleaning and organization (Harmanjit): His MLOps background suits scripting and structuring the data into clean class folders for training.
• Image annotation and class labelling (Anisha): As data engineer, she focuses on data quality, which consistent bounding boxes and labels required.
• Data augmentation (Karishma): As AI/ML Engineer, she knows how augmentation affects generalization and overfitting.

WP2 – AI Model Development and Evaluation

• Dataset splitting and training preparation (Anisha): She knows the annotated dataset best, so she can make balanced splits and prepare the YOLO configs.
• YOLOv8 and YOLOv11 model training (Karishma): Training and comparing YOLO models is core AI/ML engineering work.
• Hyperparameter tuning and model evaluation (Harmanjit): His MLOps skills suit running and tracking many experiments to compare precision, recall and mAP.
• Error analysis and model selection (Binil): He can lead the review of detection errors and document the reasoning behind the final model choice.

WP3 – Real-Time Detection and Driver Alert


• OpenCV webcam integration (Harmanjit): He has experience connecting models to real-time applications and live video.
• Real-time YOLO detection (Karishma): She trained the models, so she can best integrate them into the pipeline and tune detection.
• Audio alert generation (Binil): This self-contained feature fits his workload, and he can make sure alerts are clear for drivers.
• Streamlit interface development (Anisha): She can design a clear layout for presenting live feed and detection results.

WP4 – System Integration, Testing, and Final Demonstration

• Full system integration (Harmanjit): As MLOps Engineer, he can combine all components and manage the GitHub repository.
• Functional and scenario testing (Anisha): Her attention to detail suits testing different signs and recording issues, with a fresh view of the system.
• Performance testing (Karishma): She understands the model's metrics, so she can judge detection consistency and response time.
• Documentation and demonstration (Binil): As Project Manager, he has the full project view to compile the documents, slides and demo.

Q4: WBS Diagram

Using the descriptions in **Q1** (work packages), **Q2** (tasks), and **Q3** (task owner) organize your WBS to visually capture relevant information by way of a **tree diagram**. Your diagram should show the **hierarchical relationships** among all WPs, tasks, and it should include all relevant sub-branches. Also, make your diagram complete and coherent by enumerating the topics and by placing arrows to show all interconnected associations. Your diagram should visually display an overall summary for the workflow for your AI/ML project. You may use specialized software to make your diagram (e.g., Visio, draw.io, photoshop, etc.) [**1 mark**]

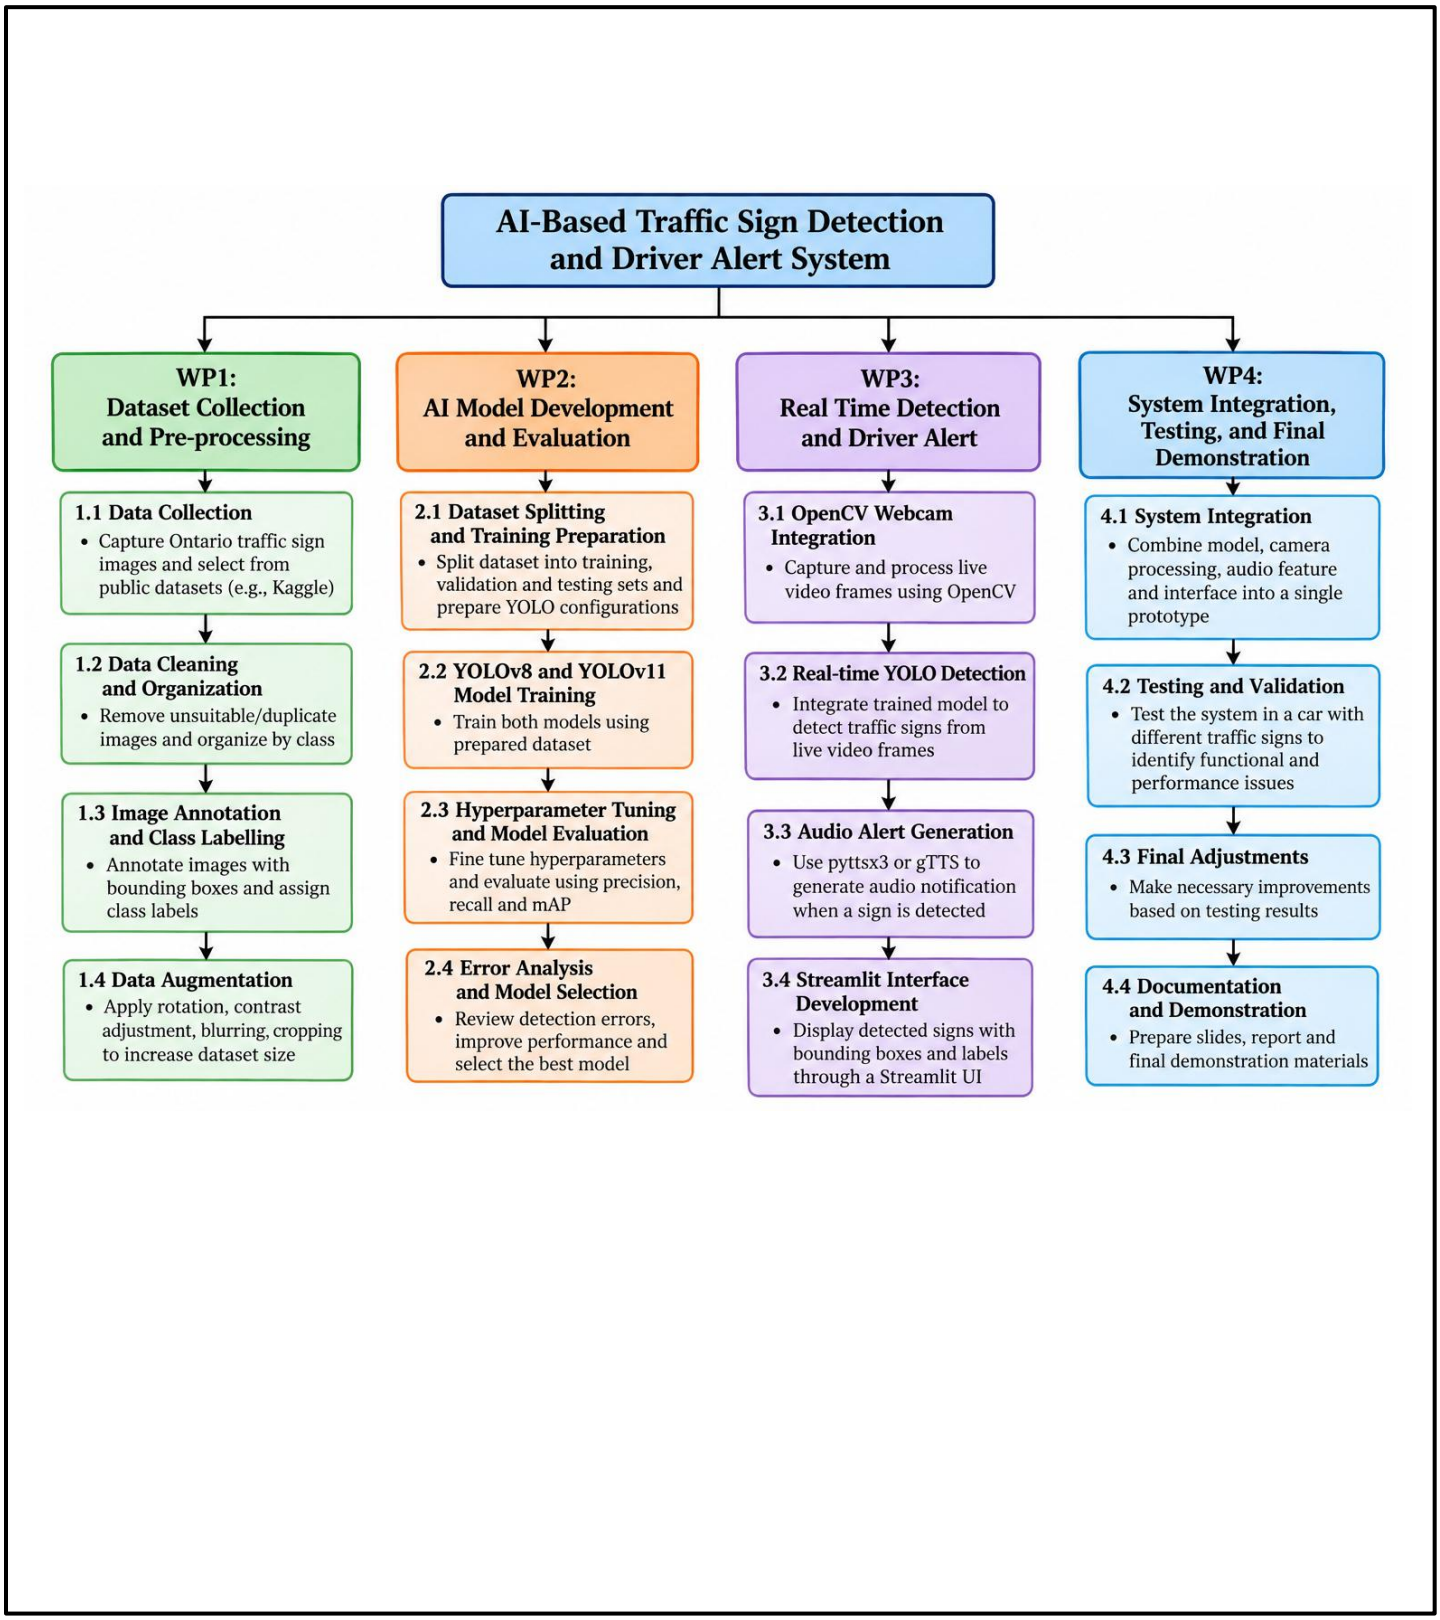

Q5: Weekly Milestones

Define **weekly milestones** and deliverables for project tracking. Your weekly milestones plan should cover Week 5 to Week 14 of the semester. Each week, you will need to complete a certain aspect of your project work (e.g., data gathering/cleaning, AI/ML modeling, model optimization, testing/prototyping, deployment/UI, tech. report writing, final presentation/demonstration). In the space below, enumerate the weeks from **Week 5 to Week 14**, and provide a **bulleted list** of the **tasks** and **sub-tasks** that you and your group aim to *realistically* accomplish by the end of each week. [**2 marks**]

Week 5: Project setup and data collection begins (WP1)
• Finalize the list of traffic sign classes to detect
.
• Start field collection of traffic sign images and shortlist relevant images for public datasets

Week 6: Data collection completed, cleaning, and annotation starts (WP1)
• Dataset collection complete and removing corrupted, duplicated and unsuitable images
• Organize images into class wise folders and agree on annotation guidelines for bounding boxes and labels
• Begin annotating the cleaned images

Week 7: Annotation, augmentation, and dataset splitting (WP1 and WP2)
• Finish annotation and start applying augmentation
• Check class balance and fix any under-represented classes
• Split the dataset into training, validation, and test set
• Prepare the YOLO data config and training parameters

Week 8: Baseline model training (WP2)
• Training baseline model YOLOv8 and YOLOv11 on the same dataset
• Notice and compare precision, recall, and mAP for both models

Week 9: Hyperparameter tuning and error analysis (WP2)
• Tune hyperparameters for both models
• Evaluate precision, recall and mAP
• Review false positives and missed detections, and identify weak classes

Week 10: Model selection and OpenCV pipeline (WP2 and WP3)
• Compare the results of both model and select best model
• Build the OpenCV webcam capture and frame-processing pipeline
• Confirm the live video feed is processed in memory and never stored

Week 11: Real-time detection and audio alerts (WP3)
• Integrate the model into the OpenCV pipeline and display bounding boxes and class labels on live frames
• Optimize frame rate and latency on the GPU-enabled setup
• Implement test to speech alerts with pyttsx3 or gTTS, triggered when a sign is detected
• Add confidence score to avoid repeating the same alert on every frame


Week 12: Streamlit interface and full integration (WP3 and WP4)
• Develop streamlit interface to show the live feed and detections
• combine the model, OpenCV pipeline, audio alert, and interface into a single system
• Fix integration bugs and merge all the part into the main GitHub branch

Week 13: System testing and refinement (WP4)
• Run functional and scenario testing with different traffic signs in different conditions
• Run in-car testing with real traffic sign
• measure the detection consistency, response time and alert clarity
• Bug fix and making final adjustments to thresholds and UI
• Start drafting the report and slides

Week 14: Final documentation and demonstration (WP4)
• Finalize the report with results and limitations
• Finish the presentation slides and prepare the demo video
Submit the final deliverables

Q6: Gantt Chart

Using the results in **Q4** (WBS diagram) and **Q5** (weekly milestones), develop a detailed **Gantt chart**. The Gantt chart is a project management tool that visually illustrates a project schedule over time. Your Gantt chart should display a list of WPs/tasks vertically while being mapped to specific task owners. A timeline is shown horizontally using "horizontal bars" should be used to represent the needed duration in weeks. Make your Gantt chart as detailed as possible. Also, important AI/ML milestones should explicitly be indicted on your Gantt chart. An example of a Gantt chart that you can replicate is show in **Appendix A**. [**2 marks**]

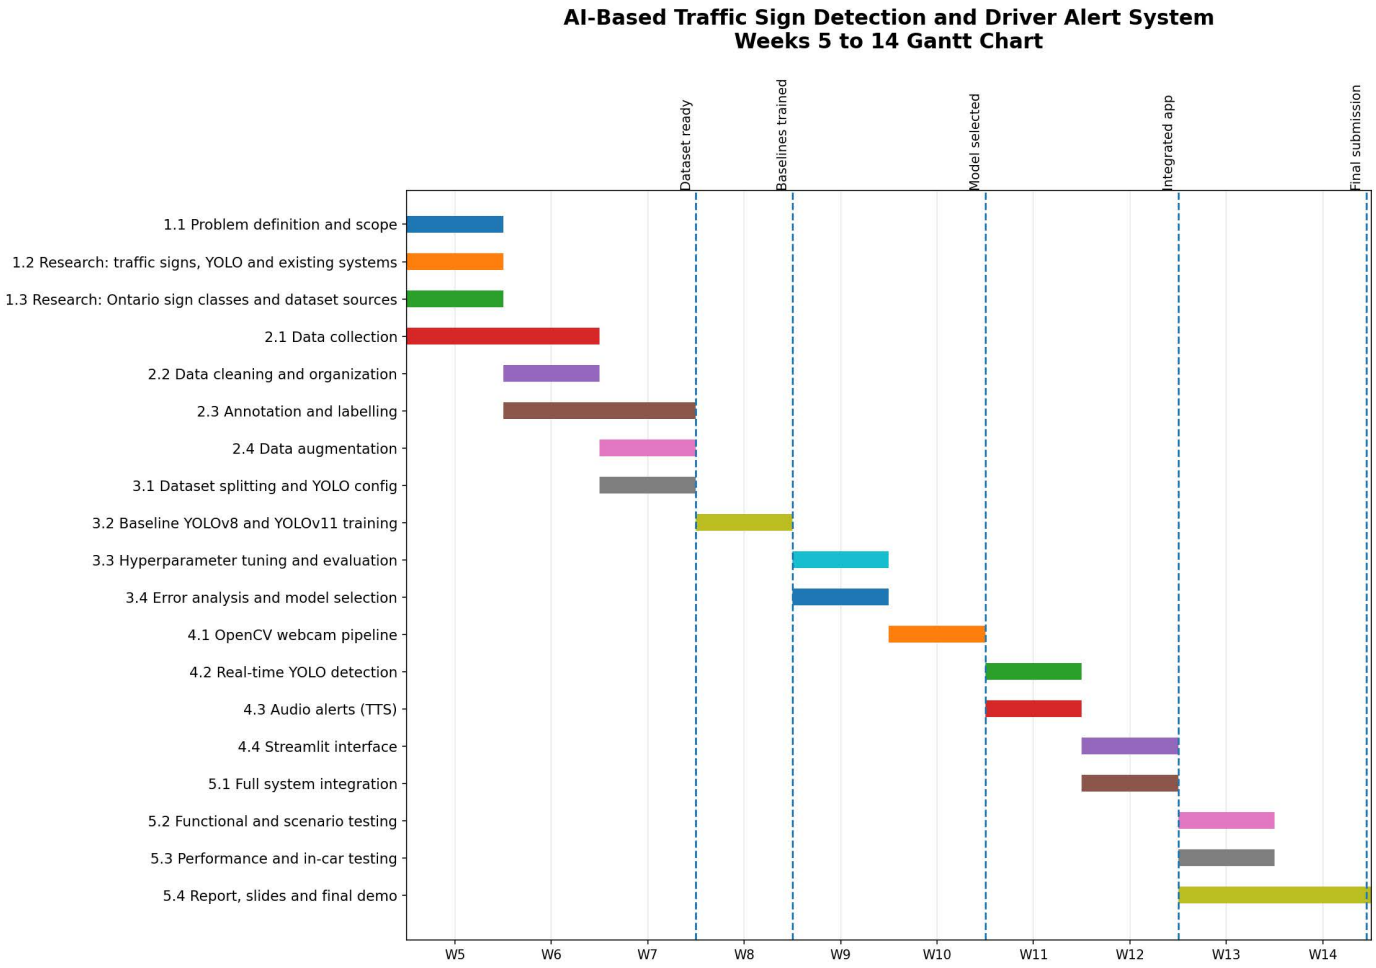

Q7: Version Control

Establish **version control practices** and **repository management protocols** with **Git/GitHub**. This tool will allow you to track changes in source code and related files over the span of your AI/ML capstone project. This tool will also allow you to practically collaborate with team members without overwriting each other's work. In the space below, explain how you intend to use Git/GitHub for version control and for repository planning. Also describe in full detail the collaboration workflow and the strategy that you aim to apply. [**1 mark**]

We will use github as the main version control and repository management tool through the project. The github repository will contain source code, dataset, docs and file management would be done by us. There are several directories like "data", "models","src","notebook," "UI" and "documentation". Team members will have an independent branch on which they can make modifications rather than editing from within a single master copy.
Collaboration process is: create a branch -> complete tasks -> make modifications -> push them on Github -> review those changes then merge it back in main branch. The team member should write a good commit message for describing what they changed and then pull up-to-date code from time intervals while working on something else. Main branch is for a fully functional version of software whereas Feature Branch is an area where developers can work on new features without affecting other parts of project.
Harmanjit is responsible for managing this repository and integrating it whereas Anisha, Karishma and Binil are contributing from their respective branch. Reviews of pull request are done prior to merge for reducing conflict and error rates. The GitHub repository would be able to back up its projects' data so that we can recover them later when needed.

Q8: Limitations, Constraints, and Risks

Identify **potential limitations, constraints, and risks** that you *may* face during this AI/ML capstone project. As you work on this question, please keep in mind that financial support from Sheridan to teams is not available, and that access this term to GPU-supported labs or clusters is not guaranteed. In the space below, develop a **risk mitigation table** that highlight the **top 5-7 risks** that you many encounter as you work on this project. Your table should also include a contingency plan for each risk. The contingency should propose a backup strategy to mitigate the potential risk, to avoid disruptions to the operations of your workflow, and to allow you to complete your AI/ML project. In the table below, provide a heading for each cell of the table that summarizes the risk and the related contingency. Then, provide a description for each cell of the table (in 2-3 sentences). [**2 marks**]

No.	Limitations, Constraints, Risks	Contingency Plan
#1	Limited computing power : Training the YOLO model may take a long time on personal laptops be cause powerful GPUs are not guaranteed.	Use google colab or lighter YOLO versions (YOLOv8n). Reduce image size and train with smaller batches if needed.
#2	Lower than expected model accuracy : The final model may not achieve the desired accuracy in real world testing.	Fine tune the model , collect more training data, and test alternative detection models if necessary.
#3	Insufficient Dataset : There may not be enough Ontario traffic sign images available for training model accurately, which could reduce the detection performance.	Use public datasets like GTSRB and mapillary along with our own images. Apply data augmentation to increase dataset size.
#4	Incorrect or inconsistent labels : Errors during annotation can reduce model accuracy.	Double check labels, review samples as a team, and correct them before training.
#5	Poor detection in bad weather or nighttime : The model may struggle in rain, fog or low-light conditions.	Include augmented images that simulate these conditions and test the model in different locations.
#6	Privacy concerns while collecting images : captured images may contain face, license plates or other identifiable information.	Review data before use and blur or remove sensitive information when necessary.
#7	Hardware /software failures : Laptop issues, lost files or software crashes may delay progress	Storing project files on GitHub and cloud storage with regular backups.

Q9: Project Outcomes

By Week 14, all teams must prepare: (*i*) **D4**, a formal **technical report** detailing the comprehensive work on the AI/ML capstone project, (*ii*) **D5a**, **slide presentation** of the technical report, and (*iii*) **D5b**, a **working live demonstration of the AI/ML solution**.

Q9.1 – What do you anticipate the major outcomes of your capstone project will be?

Q9.2 – What type of AI/ML method will your solution consider (i.e., regression, classification, clustering, or possibly a combination of different methods)?

Q9.3 – What type of UI/system will you have to showcase a working demonstration of your AI/ML solution (e.g., MobileApp, cloud service, locally/publicly hosted URL, AI-powered physical system – IoT, drone, or robot, or possibly a combination of various UI/systems)?

In the space below, provide specific answers to these three questions to demonstrate that your anticipated capstone results are *thoroughly considered* and *strategically* planned. [**2 marks**]

9.1 – Major Outcomes

The major outcome of our capstone project will be a working AI based traffic sign detection and driver alert system that is capable of detecting specific traffic signs from a live camera feed and gives alert to the driver about the sign. The system will use a trained YOLO object detection model to identify the signs and display the detected signs with bounding boxes and class labels.
The project will also make a comparison between YOLOv8 and YOLOv11 using precision, recall and mAP as the evolution matrices. The completed system will be integrated with selected YOLO model with OpenCV for Realtime video processing , streamlit for user interface, and pyttsx3 or gTTS for audio alerts. The system will be tested using different traffic signs and real world scenarios to evaluate detection consistency, response time, and alert clarity. The final outcomes will include the working prototype, testing results, GitHub repository, technical report, presentation, and live demonstration.

9.2 – AI/ML Method

The project used supervised learning for object detection and image classification. The AI/ML method will be object detection using YOLO models, specifically YOLOv8 and YOLOv11. The custom traffic sign dataset will be divided into training, validation, and testing sets. The model will be trained using annotated traffic sign images containing bounding boxes and class labels. YOLOv8 and YOLOv11 will be trained and compared using precision, recall, and mean Average Precision. Hyperparameters will be adjusted to improve the performance of the models. False positives and missed detections will also be analyzed to identify weaknesses. Based on these results, the better-performance model will be selected for the final real-time traffic sign detection

Q9.3 – UI/System for Demonstration

The final demonstration will combine webcam. OpenCV and a streamlit based user interface. The camera will provide live feed and OpenCV will process the income frame with the YOLO model for detection. The streamlit interface will display the live feed with the detected signs, bounding boxes and class labels. When a sign is detected, a test-to-speech system will generate audio alert describing that sign. The final demonstration will be performed using a webcam and GPU enabled environment with the system tested using different traffic sign and , where possible inside a car.

References (Include 12-15 peer-reviewed sources to back your AI/ML capstone project ideas cited above with your answers. You may reuse references from "**D1 – Project Proposal**").

1. A. M. Jenifer and R. Balamanigandan, "Advanced Road Sign Detection Techniques: Leveraging Harris Corner Detector for Robust Recognition," 2024 4th International Conference on Soft Computing for Security Applications (ICSCSA), Salem, India, 2024, pp. 345-350, doi: 10.1109/ICSCSA64454.2024.00061.
2. Y. Zhu, "Road Traffic Sign Detection Algorithm Based on Improved YOLOv8n," 2026 7th International Seminar on Artificial Intelligence, Networking and Information Technology (AINIT), Dalian, China, 2026, pp. 755-758, doi: 10.1109/AINIT70033.2026.11557703.

[3] R. Tarun and B. P. Esther, "Real-time regional road sign detection and identification using Raspberry Pi," 2023 International Conference on Networking and Communications (ICNWC), Chennai, India, 2023, pp. 1-5, doi: 10.1109/ICNWC57852.2023.10127370

[4] N. U. H D, A. B N, Y. N and M. Ruj, "Real-Time Traffic Sign Detection and Recognition for Enhanced Road Safety in Autonomous Driving: A Deep CNN-Based Approach," 2023 Fourth International Conference on Smart Technologies in Computing, Electrical and Electronics (ICSTCEE), Bengaluru, India, 2023, pp. 1-4, doi: 10.1109/ICSTCEE60504.2023.10584947.

[5] P. S. Gade, S. L. Shinde, S. B. Kolapkar, A. V. Walte, S. K. Sharma and R. D. Chintamani, "Traffic Sign Board Recognition and Alert System Using R-CNN," 2023 4th International Conference on Computation, Automation and Knowledge Management (ICCAKM), Dubai, United Arab Emirates, 2023, pp. 01-05, doi: 10.1109/ICCAKM58659.2023.10449516.

[6] W. H. D. Fernando and S. Sotheeswaran, "Automatic road traffic signs detection and recognition using 'You Only Look Once' version 4 (YOLOv4)," 2021 International Research Conference on Smart Computing and Systems Engineering (SCSE), Colombo, Sri Lanka, 2021, pp. 38-43, doi: 10.1109/SCSE53661.2021.9568285.

[7] B. Wang and G. Wang, "A Lightweight Model for Road Sign Detection Based on Improved-YOLOv8," 2024 9th International Conference on Electronic Technology and Information Science (ICETIS), Hangzhou, China, 2024, pp. 319-322, doi: 10.1109/ICETIS61828.2024.10593701.

[8] S. Ashwath, C. T, A. S. M, S. S and S. D R, "Enhancing Road Safety through Innovative Traffic Sign Detection and Recognition with YOLOv5," 2024 International Conference on Intelligent and Innovative Technologies in Computing, Electrical and Electronics (IITCEE), Bangalore, India, 2024, pp. 1-4, doi: 10.1109/IITCEE59897.2024.10467719.

[9] N. Bhatt, P. Laldas and V. B. Lobo, "A Real-Time Traffic Sign Detection and Recognition System on Hybrid Dataset using CNN," 2022 7th International Conference on Communication and Electronics Systems (ICCES), Coimbatore, India, 2022, pp. 1354-1358, doi: 10.1109/ICCES54183.2022.9835954.

[10] Y. Setiawan, M. N. Puji and W. Astuti, "Traffic Signs Detection System Using YOLO (You Only Look Once) That Provides Notification," 2024 IEEE International Conference on Smart Mechatronics (ICSMech), Yogyakarta, Indonesia, 2024, pp. 95-100, doi: 10.1109/ICSMech62936.2024.10812285.

[11] L. Qiu, "Real-Time Traffic Sign Detection System for Autonomous Driving Based on YOLO Algorithm," 2024 Cross Strait Radio Science and Wireless Technology Conference (CSRSWTC), Macao, China, 2024, pp. 1-4, doi: 10.1109/CSRSWTC64338.2024.10811588.

[12] Tian and J. Xiong, "A Lightweight Real-Time Traffic Sign Detection Model Based on Improved YOLOv8n," 202544th Chinese Control Conference (CCC), Chongqing, China, 2025, pp. 8501-8506, doi: 10.23919/CCC64809.2025.11178591.

WBS Number	Task Title	Task Owner	Start Date	Due Date	Duration	% of Task Complete	Phase One														Phase Two					
							Week 1					Week 2					Week 3					Week 4					W
							M	T	W	R	F	M	T	W	R	F	M	T	W	R	F	M	T	W	R	F	M
1	Project Conception & Initiation																									
1.1	Project Charter	Leon W	3/12/55	3/15/55	3	100%																				
1.1.1	Project Charter Revisions	Kylie R	3/15/55	3/16/55	1	100%																				
1.2	Research	Pete S	3/15/55	3/21/55	6	90%																				
1.3	Projections	Steve L	3/16/55	3/22/55	6	40%																				
1.4	Stakeholders	Allen W	3/17/55	3/22/55	5	70%																				
1.5	Guidelines	Malik M	3/18/55	3/22/55	4	60%																				
1.6	Project Initiation	Malik M	3/23/55	3/23/55	0	50%																				
2	Project Definition & Planning																									
2.1	Scope & Goal Setting	Steve L	3/24/55	3/28/55	4	5%																				
2.2	Budget	Allen W	3/29/55	4/2/55	4	30%																				

Good Luck!
